


JING-ZHANG OPERATING LAYER ON APPROVED CONTEXT

Planning is the credible base; the civic cross and stations are the design protagonists

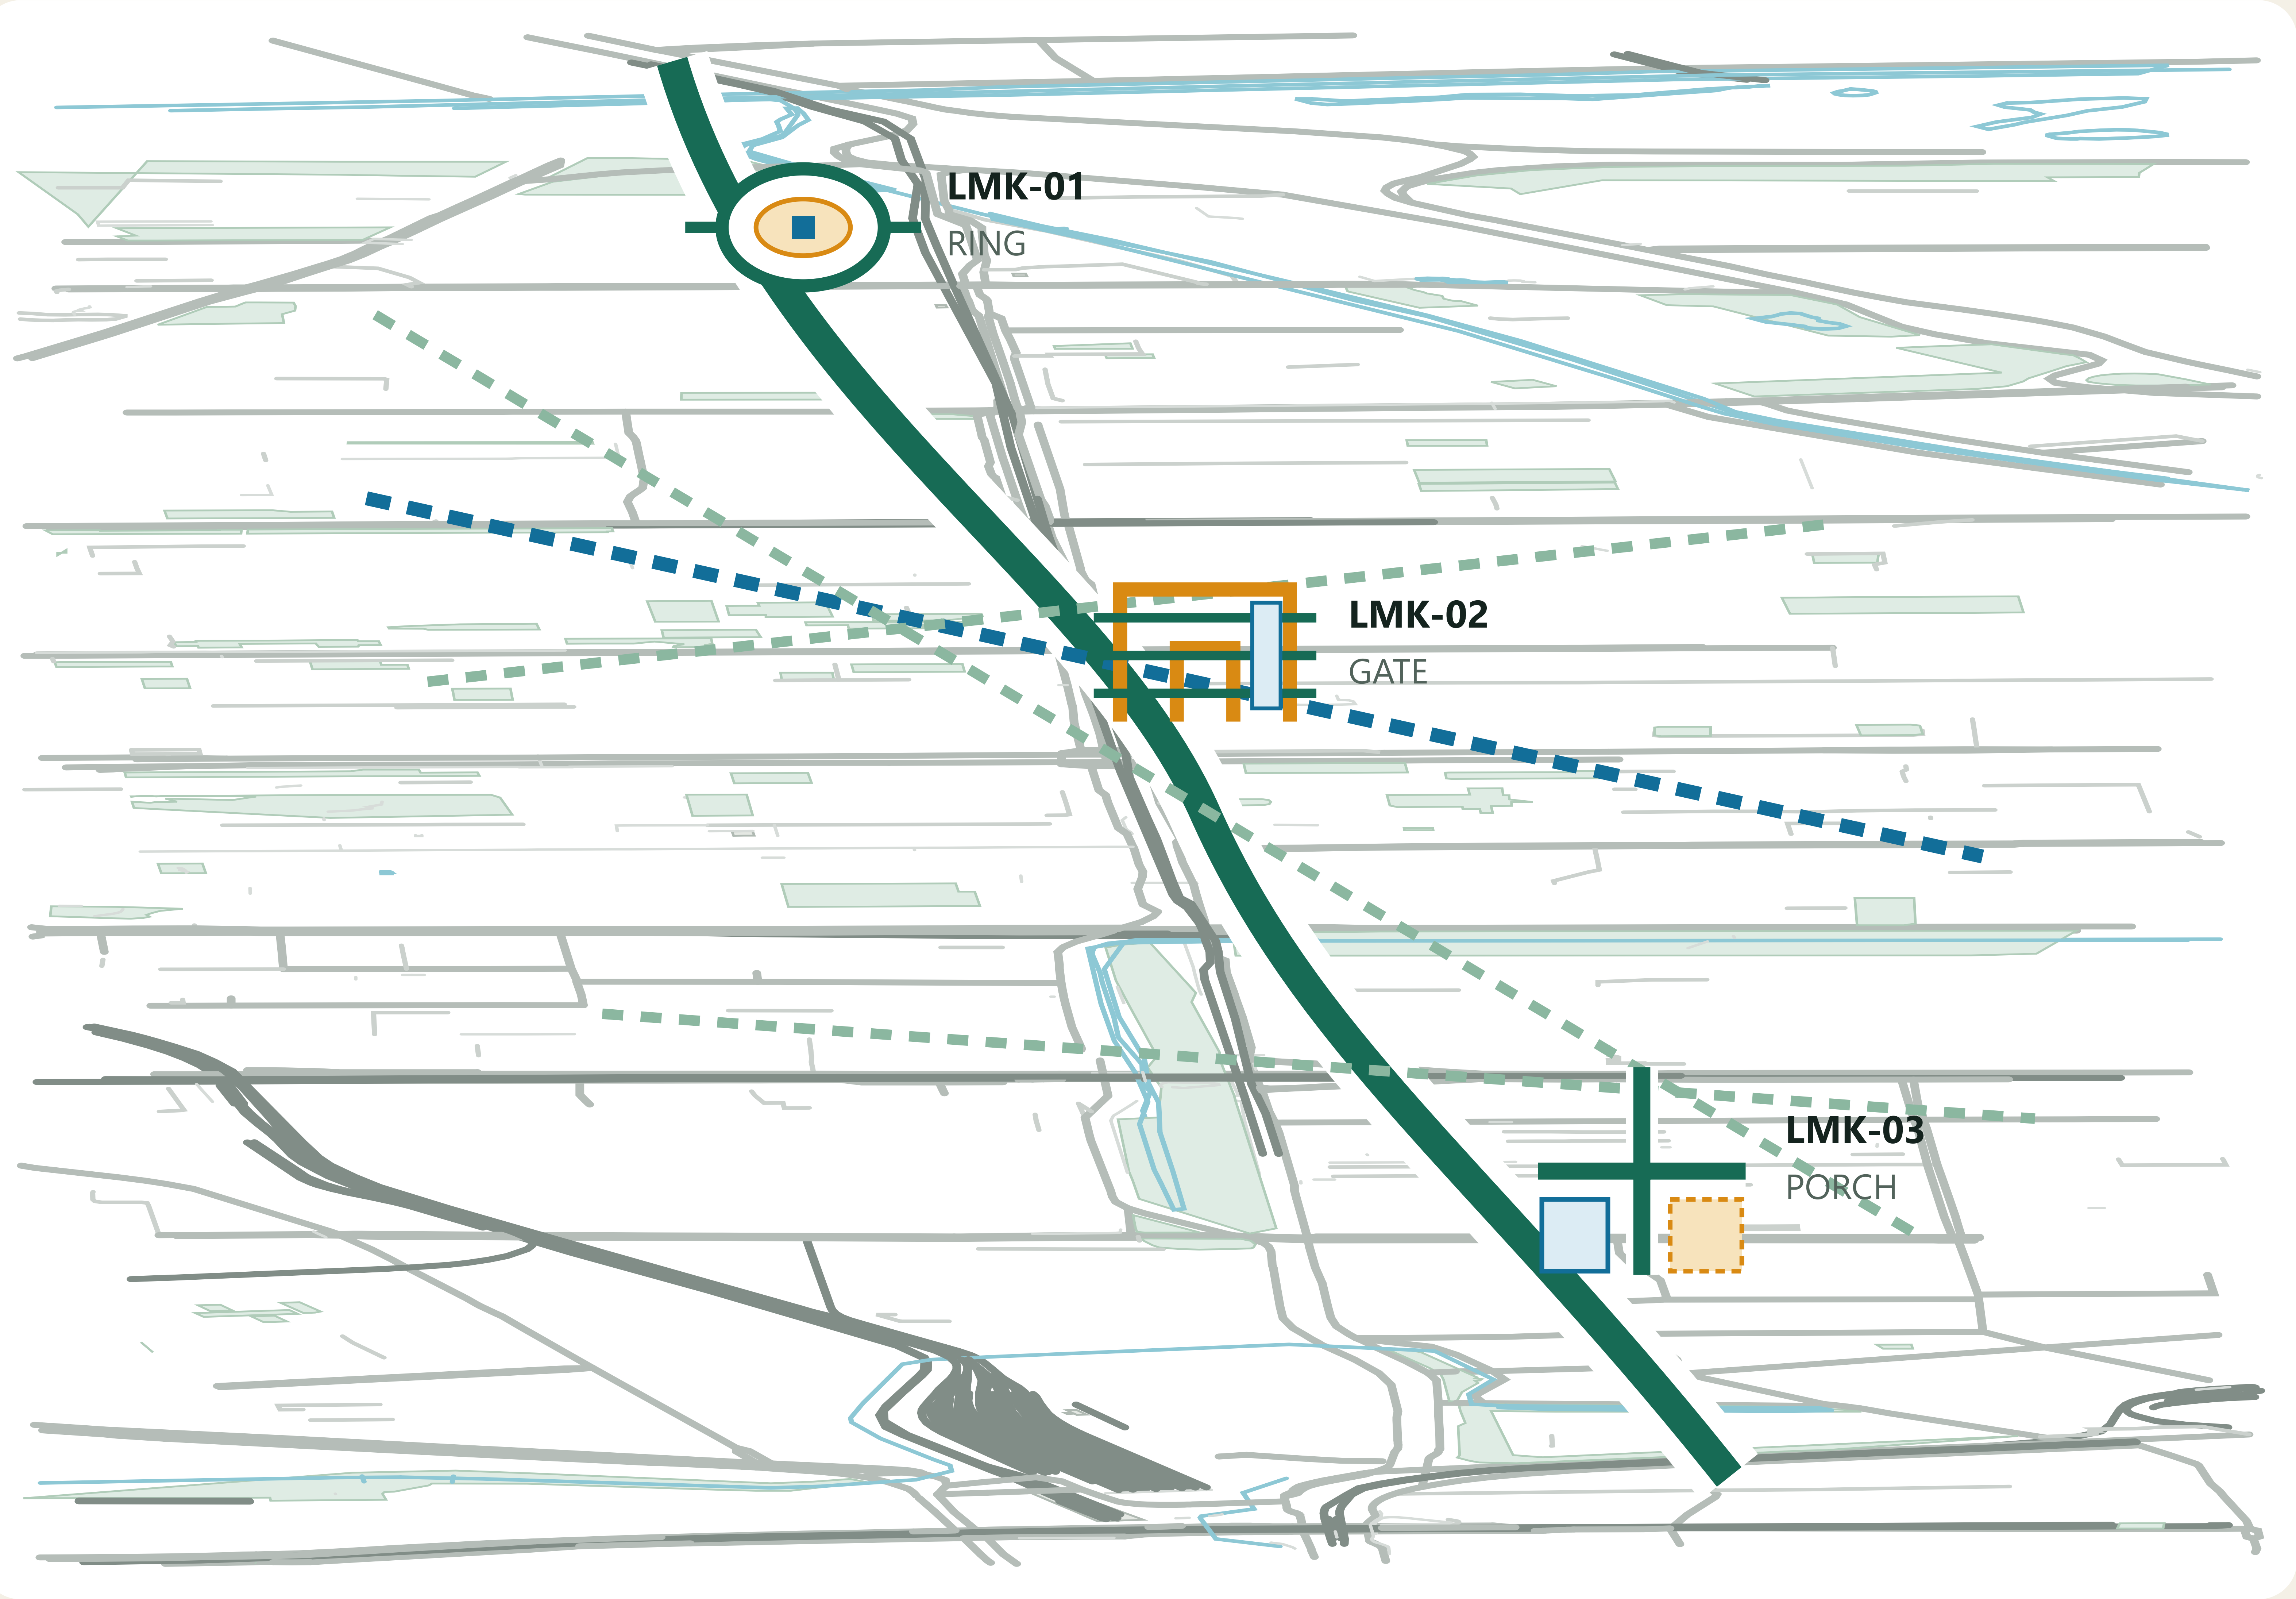

PUBLISHED GREEN BELT

spine/stations/wings = stoppable, removable overlay

EXISTING / PUBLISHED

9 km belt, slow-mobility links, Dazhongsi centre

DESIGN PROPOSAL

4 m route, one-side bay, staffed Porch

INTERFACE WINDOWS

Ring bypass / Gate passage / Porch cross

UNKNOWN


survey, title, entrances, utilities, permits

Map data © OpenStreetMap contributors · ODbL · 2026-08-13




ORDINARY OPEN DAY

CONCEPT-GENERATED / NOT FIELD EVIDENCE; use vector model for dimensions

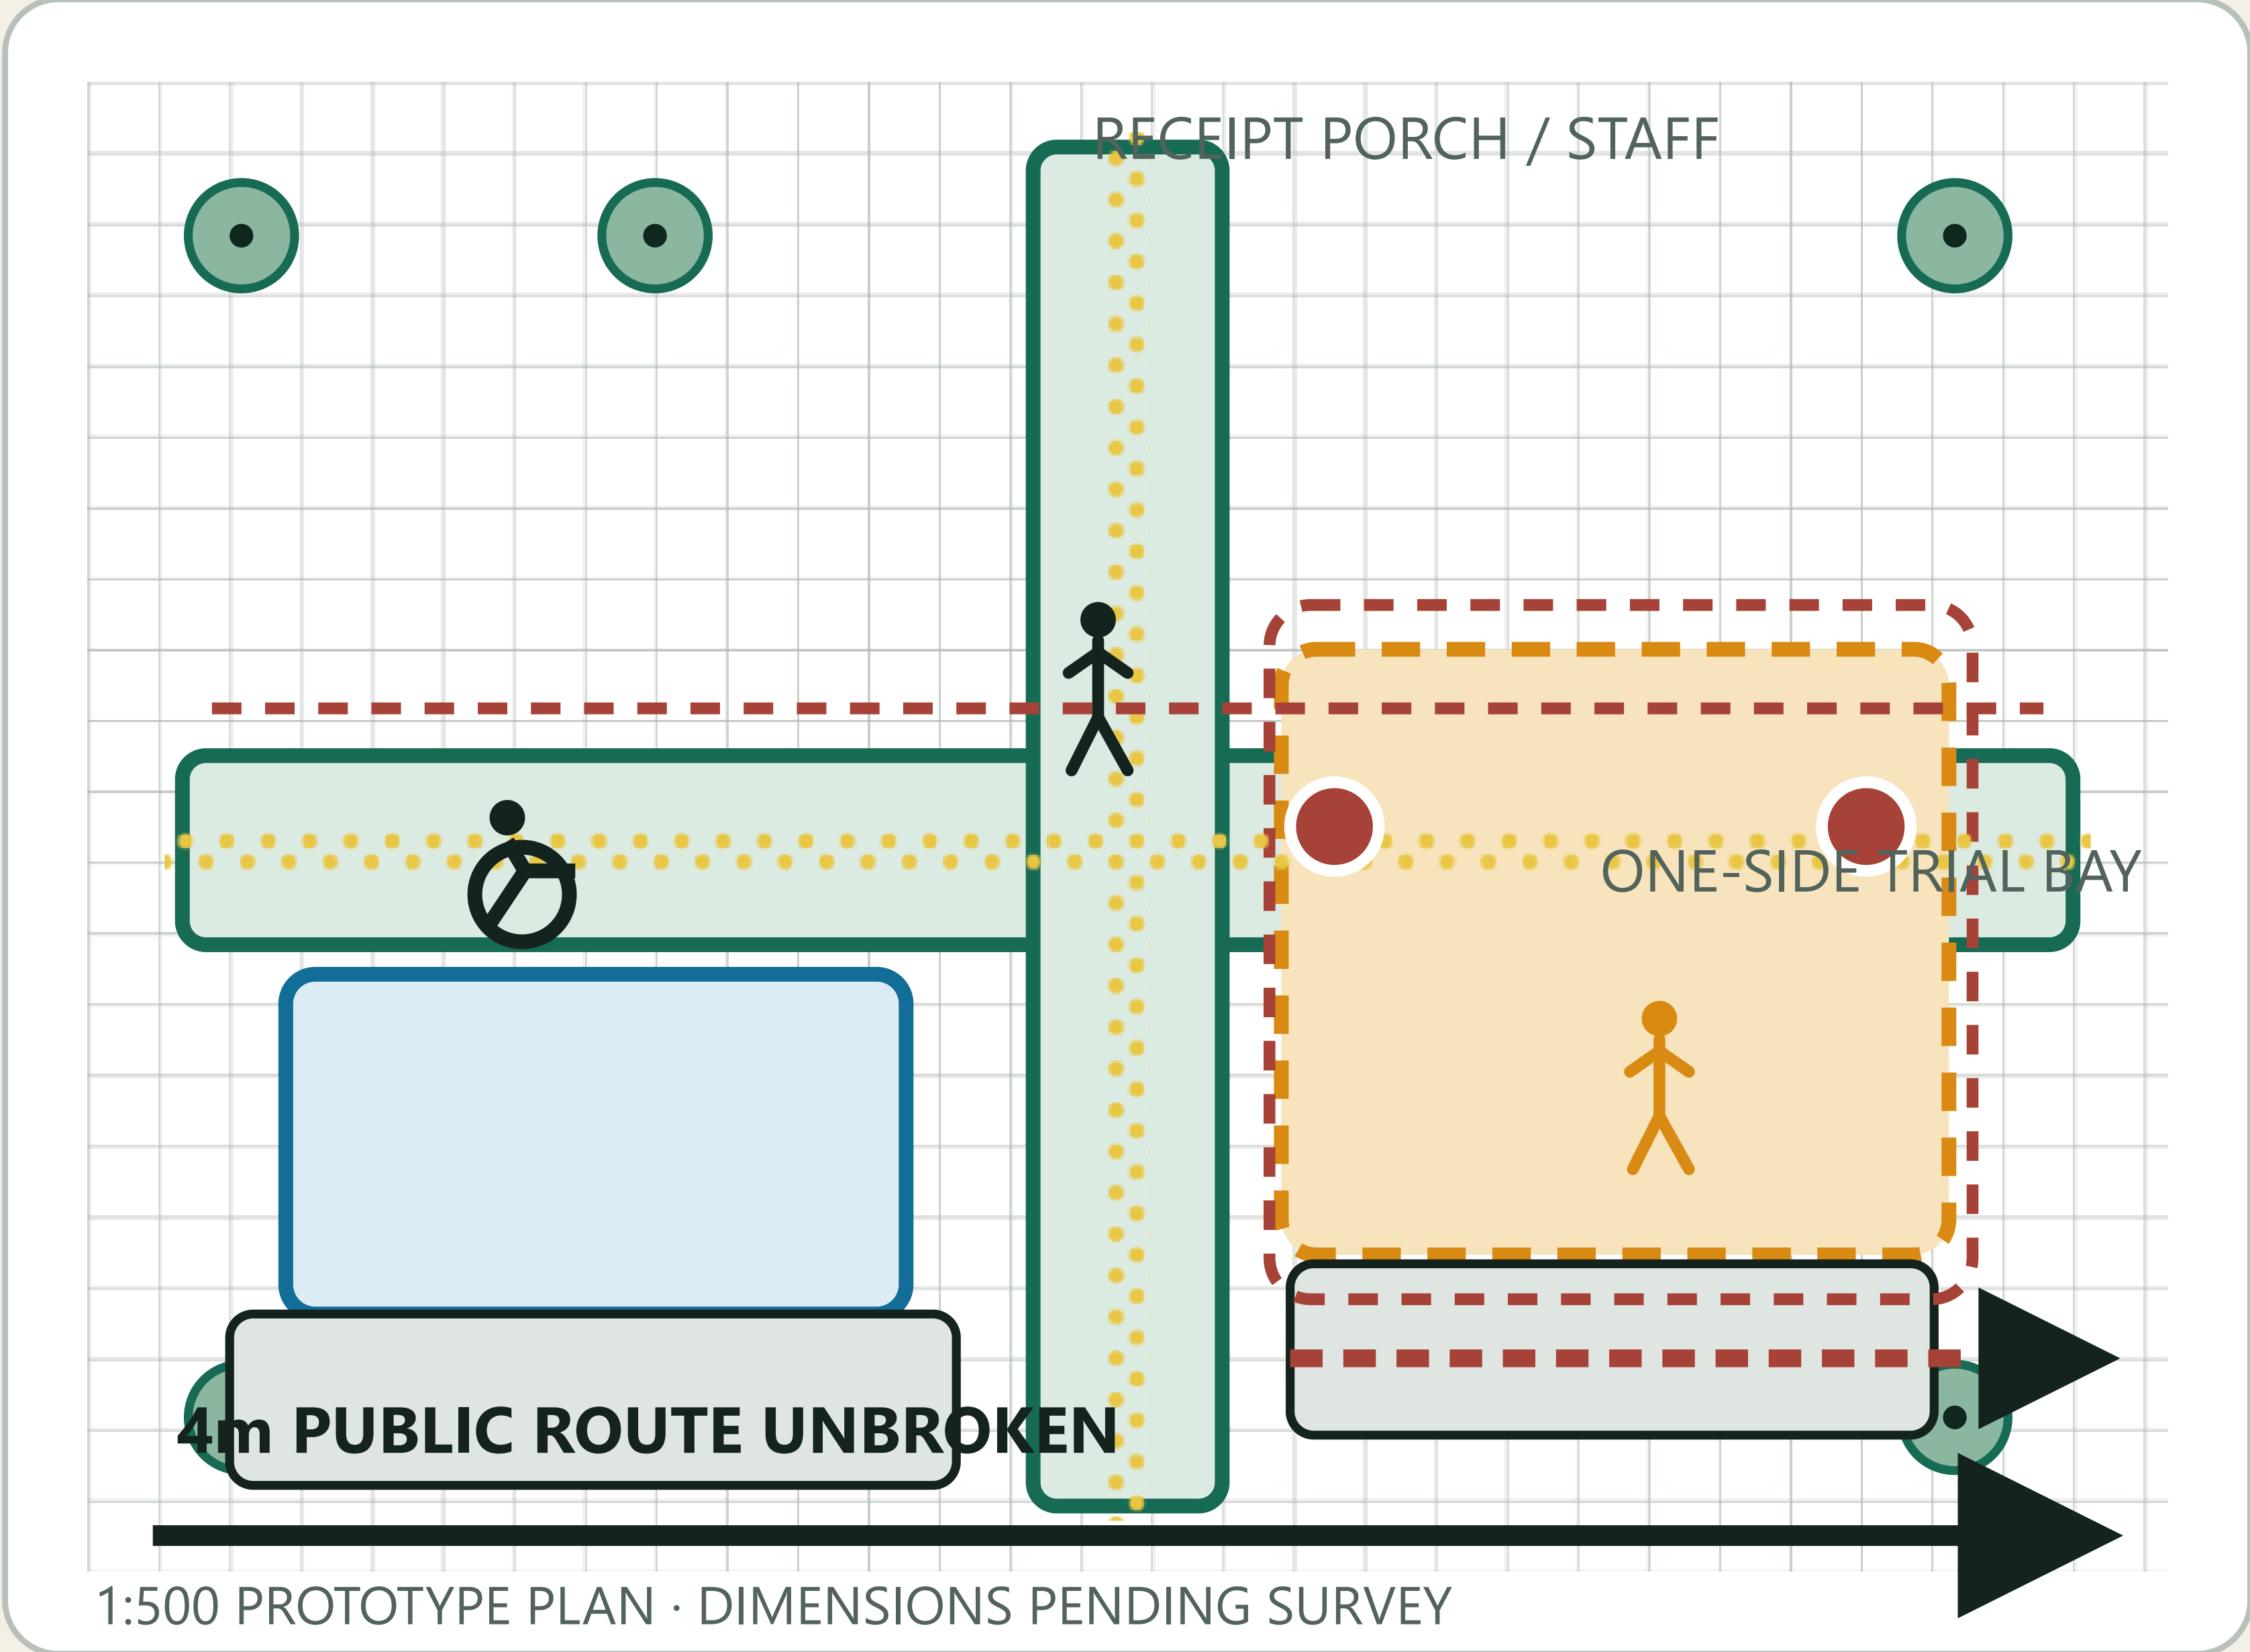


ONE SPATIAL MODEL • LAYERED CUTAWAY ASSEMBLY

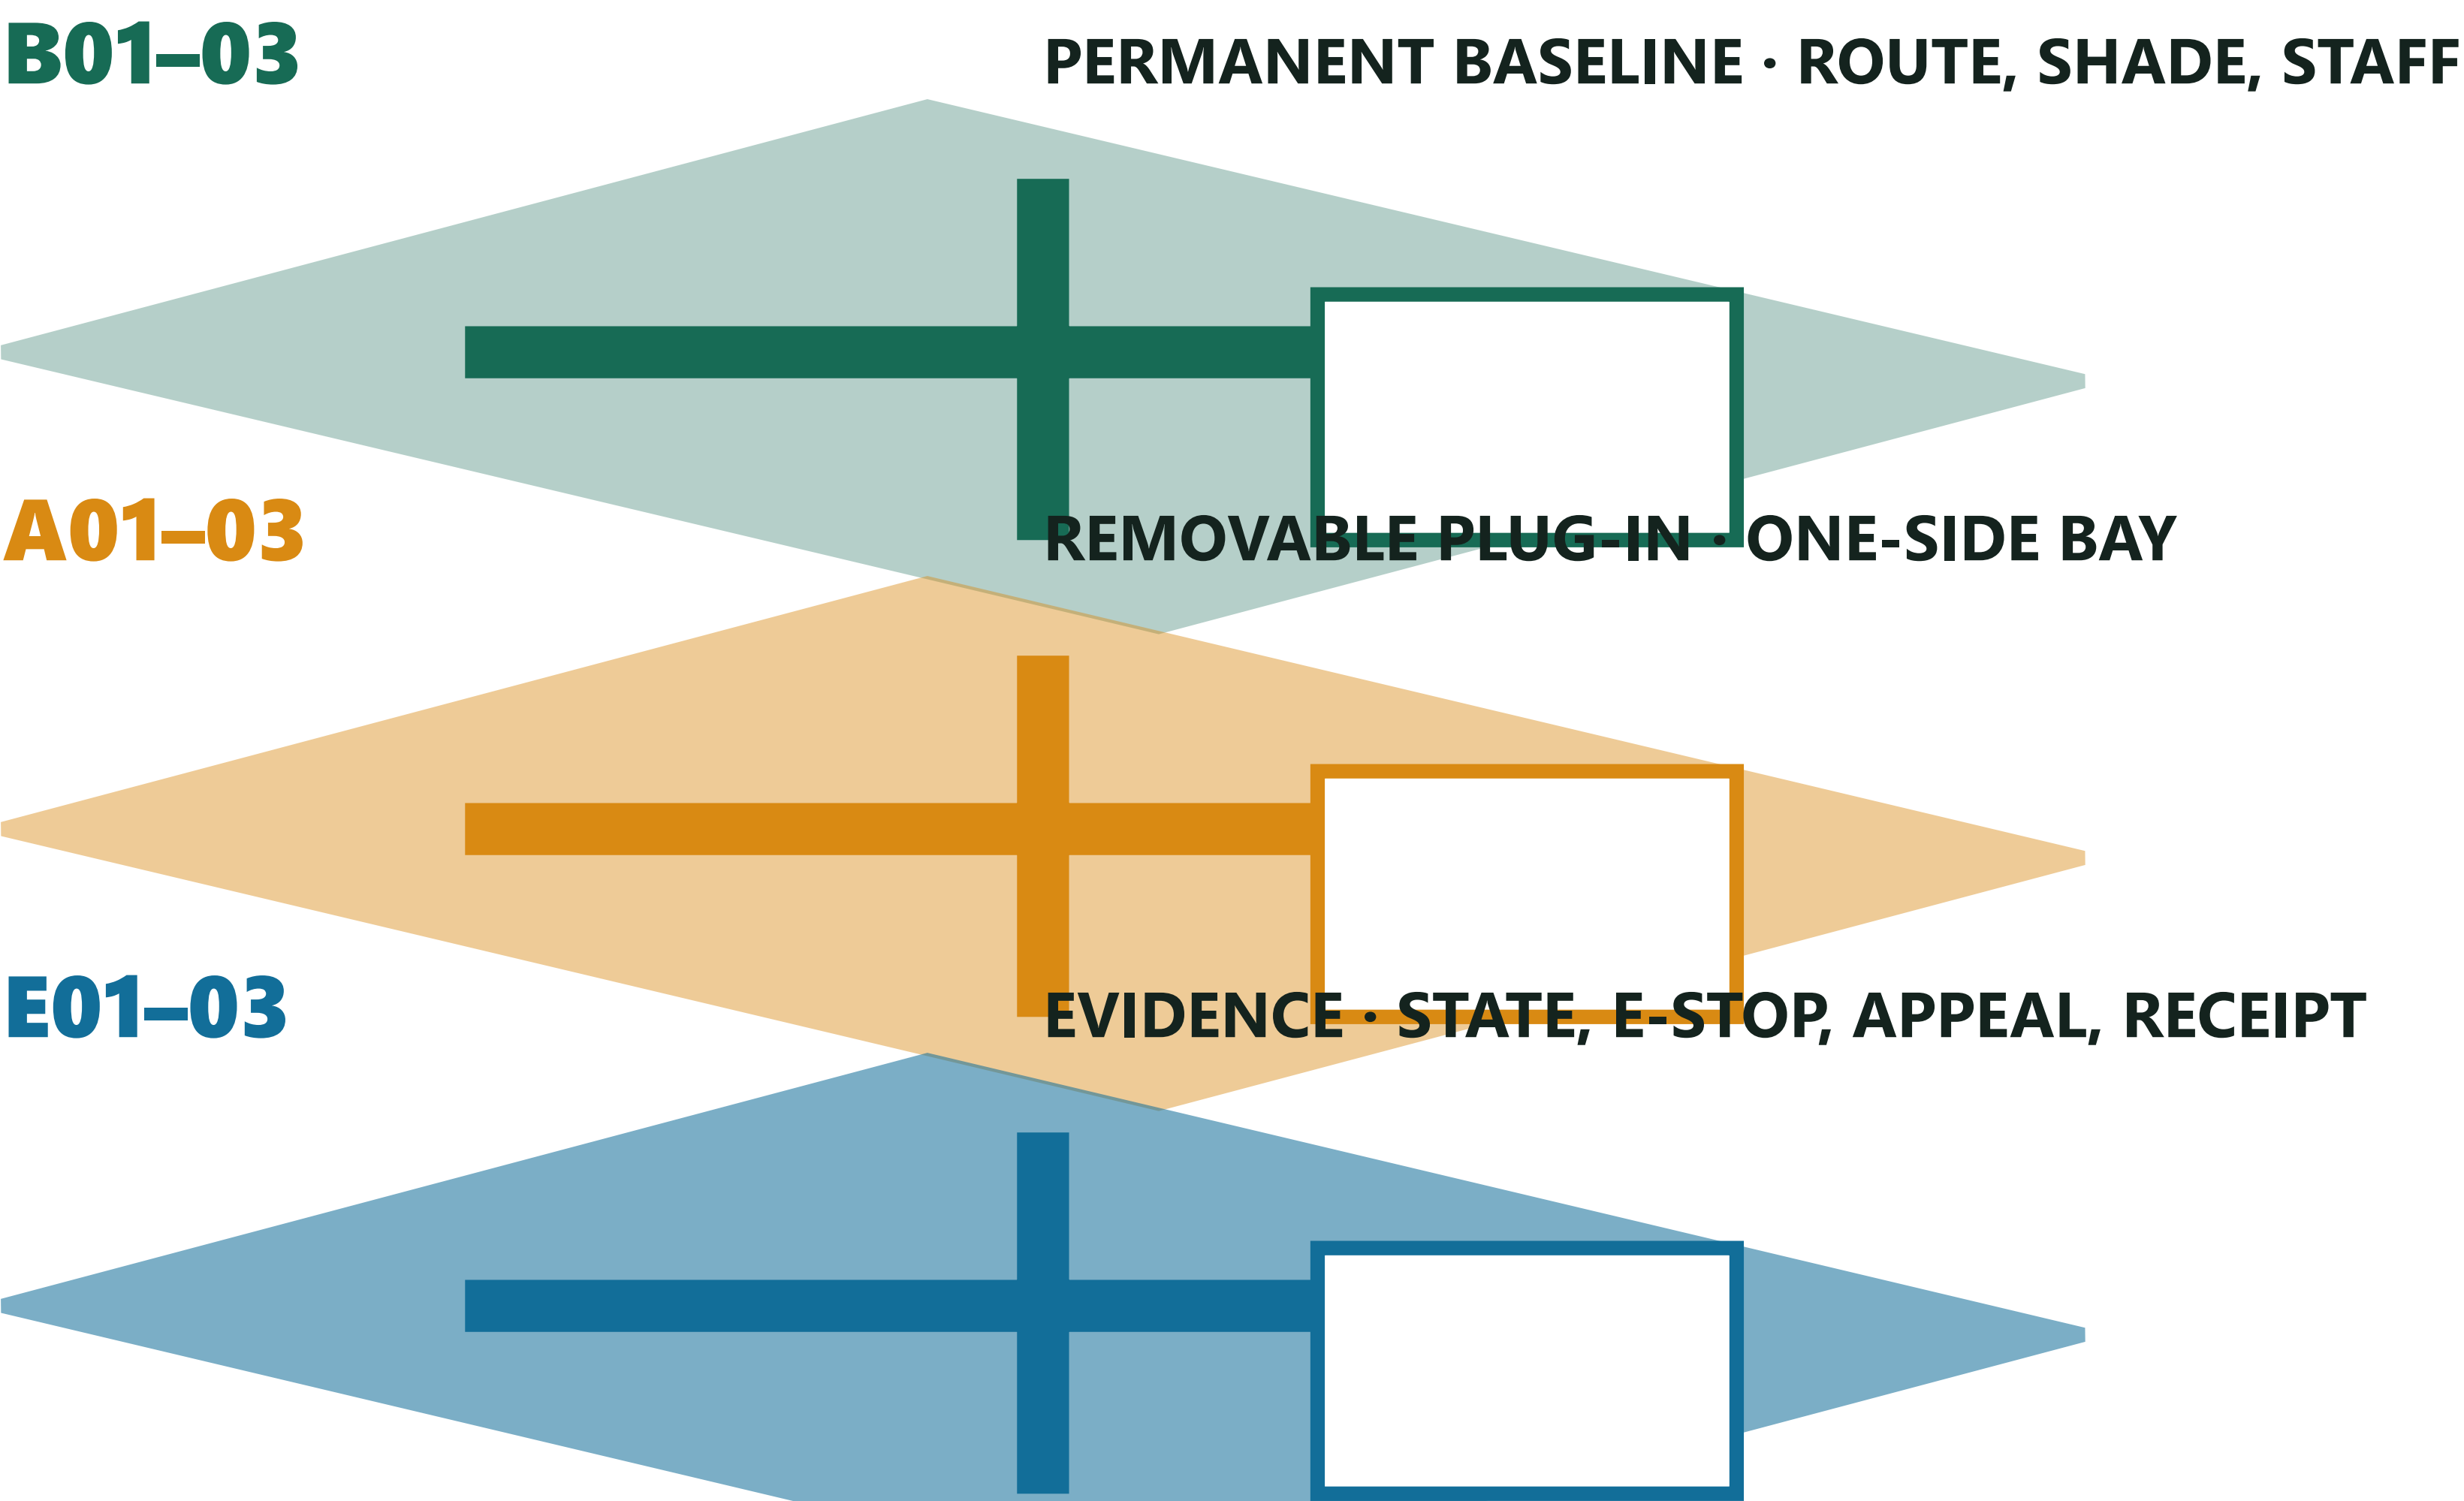



RETIRE: plug-ins leave by service route; route, shade, staffed service and evidence panel remain

TRIAL DAY • PUBLIC-BUFFER-BAY-PORCH

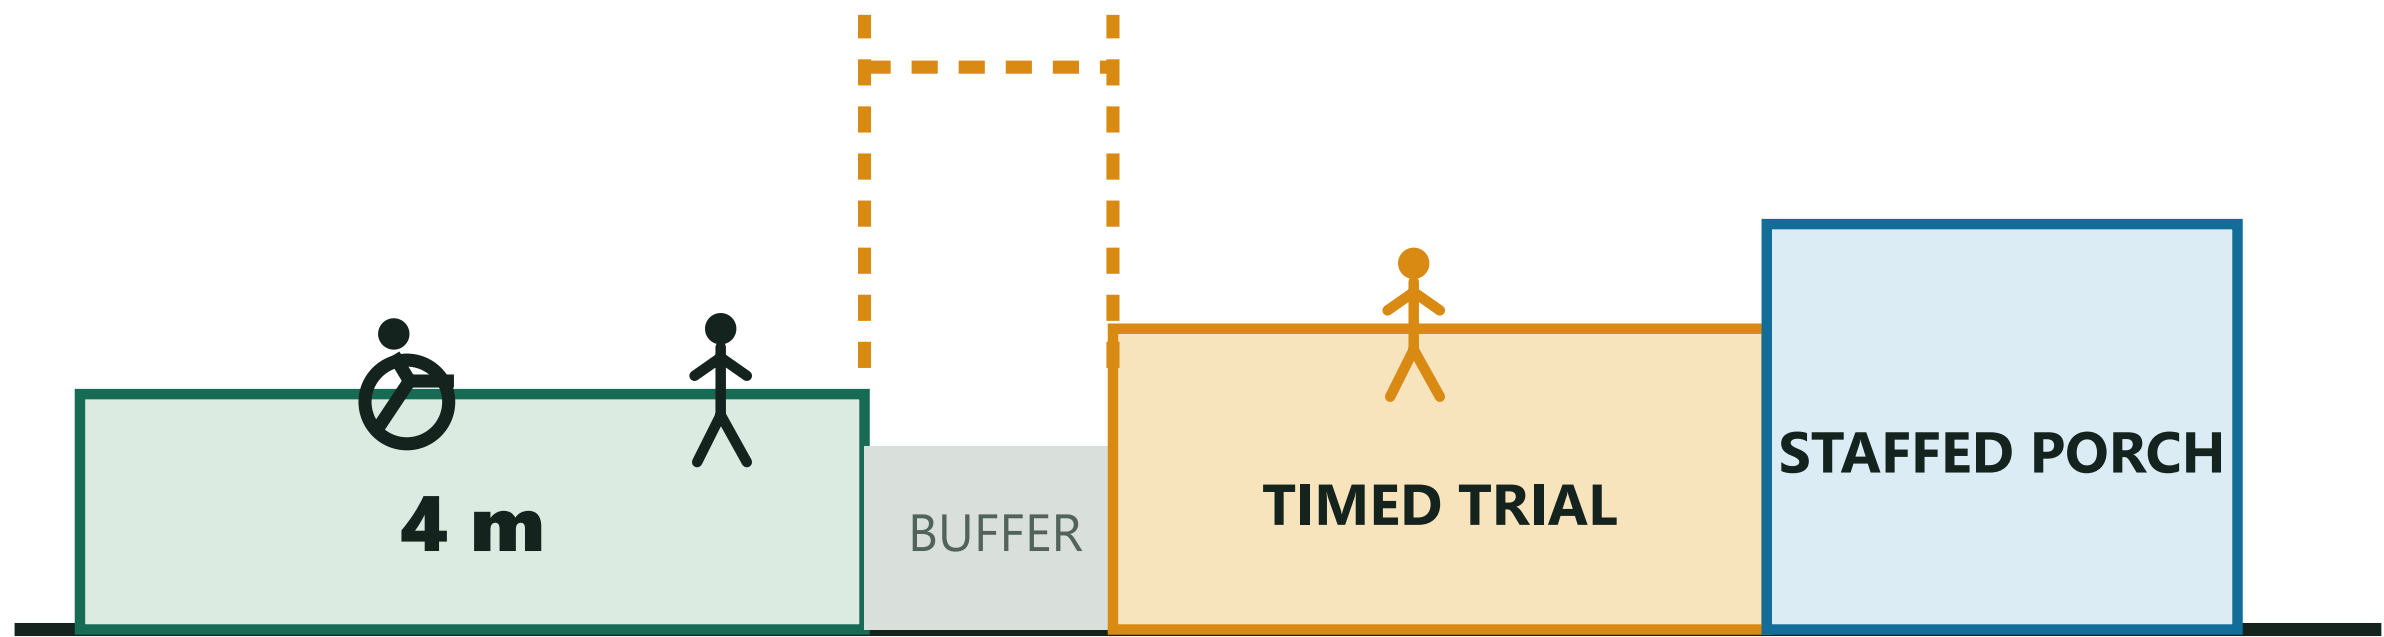

Structure, clearance, drainage, fire and durability are prototype assumptions pending review

1:50 / 1:20 REVERSIBLE NODES • PUBLIC LAYER FIRST

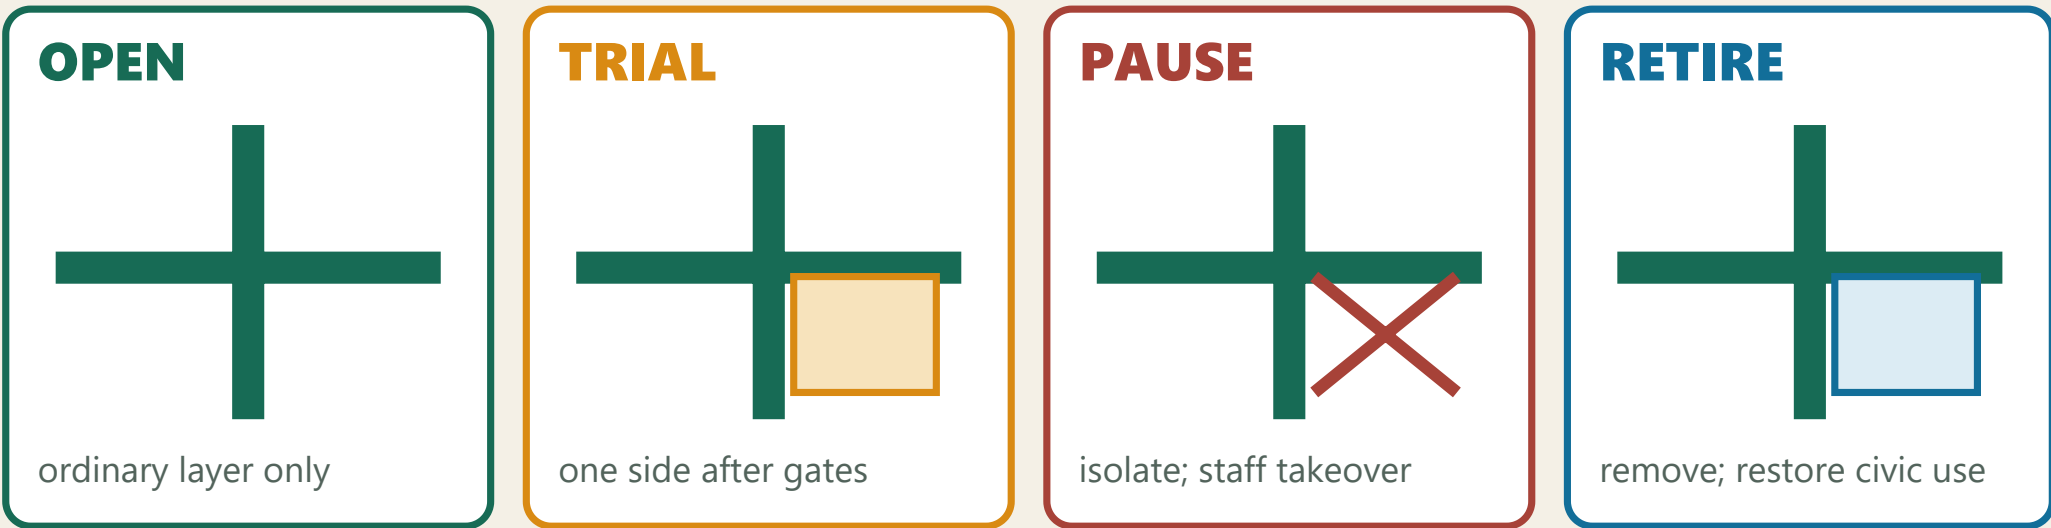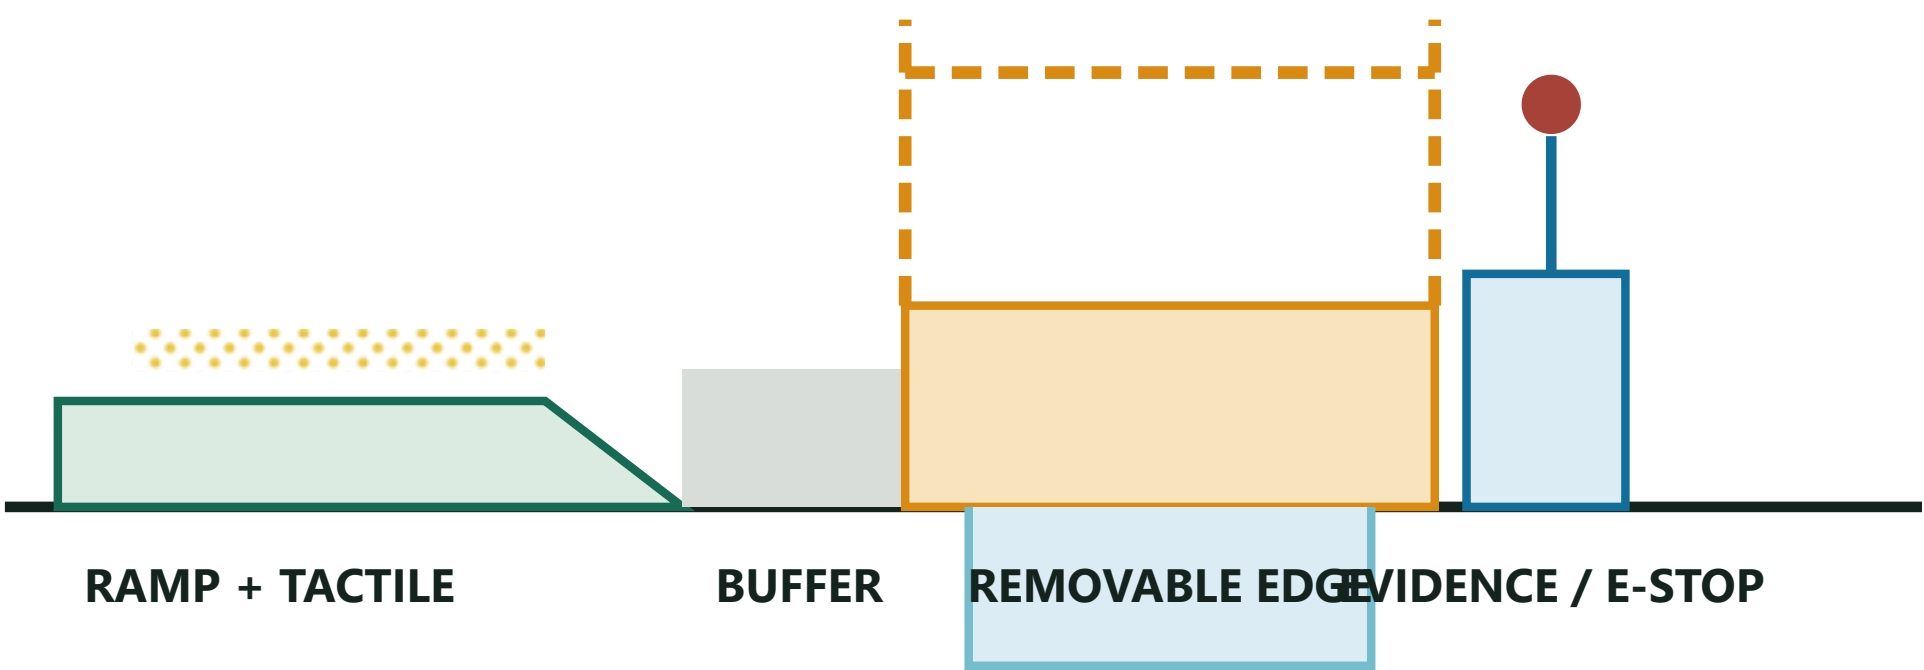

ONE YARDSTICK • THREE OPTIONS, ONE PUBLIC REJECTION

ALT-A

CENTRAL MIXING

1:500 PROTOTYPE PLAN - DIMENSIONS PENDING SURVEY

REJECT • CUTS PUBLIC CROSS

Hard conflict among public, fire and removal routes.

ALT-B

SPLIT BAYS

1:500 PROTOTYPE PLAN - DIMENSIONS PENDING SURVEY

REVISE • FRAGMENTED CONTROL

Routes remain but posts and exit are dispersed.

ALT-C

ONE-SIDE BAY

1:500 PROTOTYPE PLAN - DIMENSIONS PENDING SURVEY

ADVANCE • ROUTE CONTINUOUS

AI is concentrated; posts, e-stop and exit are reachable.

OPEN

ordinary layer only

TRIAL

one side after gates


PAUSE

isolate; staff takeover

RETIRE

remove; restore civic use

ORDINARY DAY • ROUTE, WAITING + STAFFED SERVICE

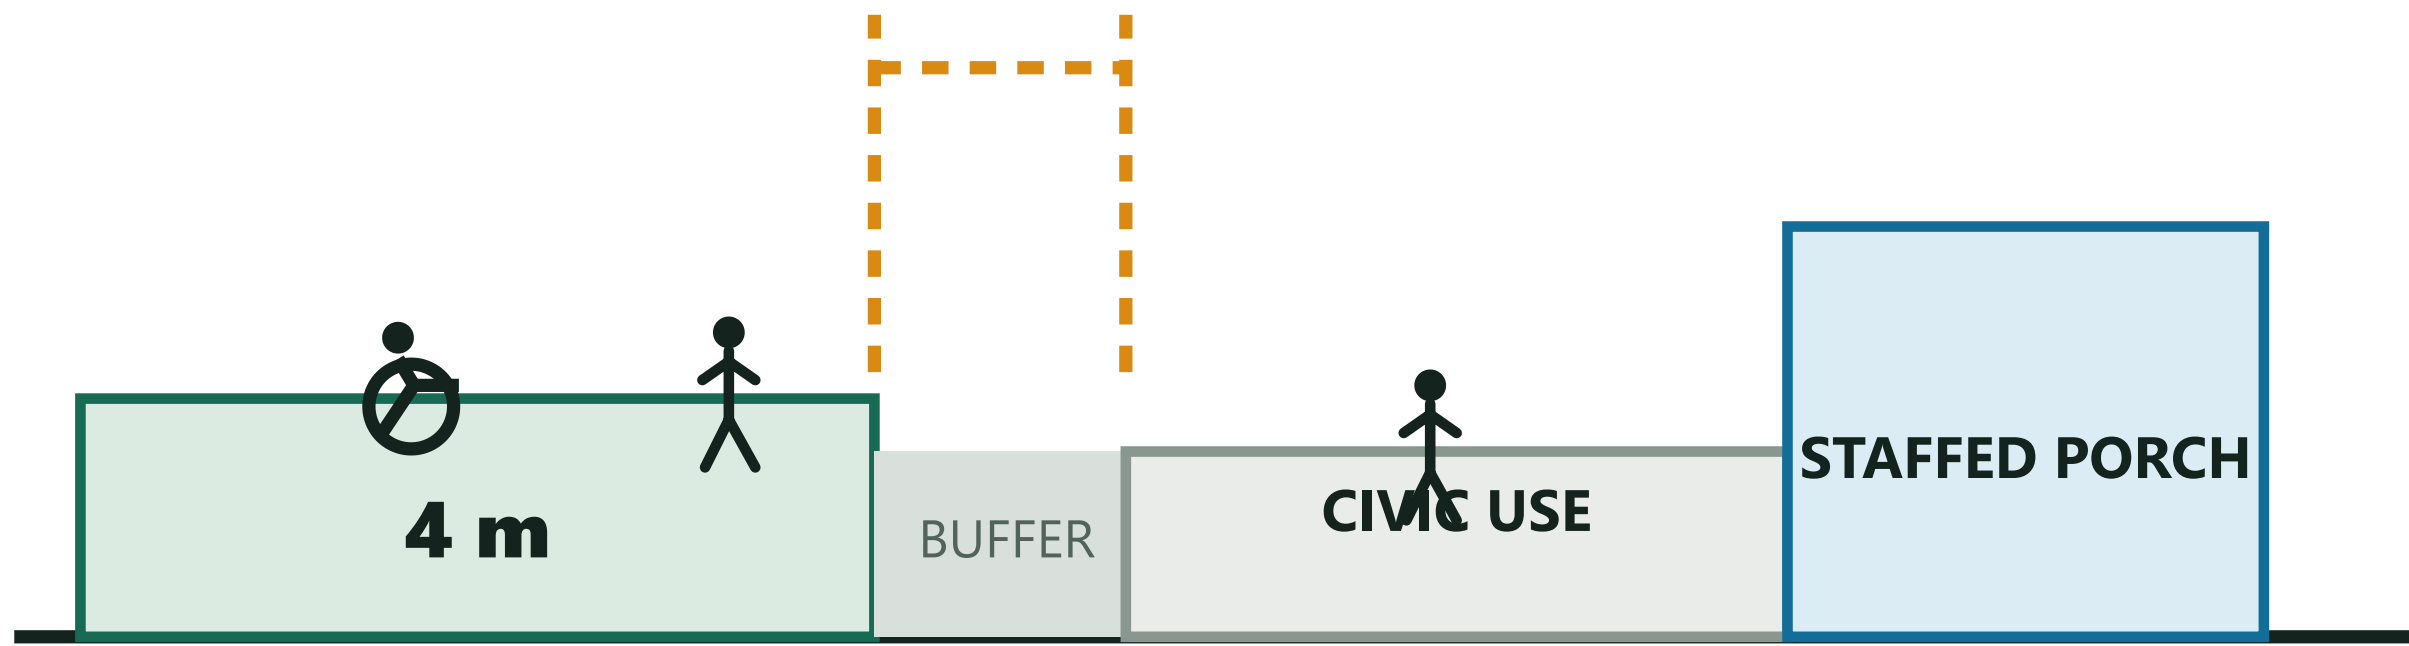

Structure, clearance, drainage, fire and durability are prototype assumptions pending review

ORDINARY OPEN DAY FIRST • 90 DAYS ARE FIVE ENTRY GATES

DAY 0–15

survey/title/entrance/utility/fire

FAIL → DO NOT ADVANCE

DAY 16–30

build public route/waiting/shade/staff only

FAIL → DO NOT ADVANCE

DAY 31–45

record 7 ordinary operating days

FAIL → DO NOT ADVANCE

DAY 46–75

timed trial after permits + posts

FAIL → DO NOT ADVANCE

DAY 76–90

stop drill/removal/public receipt

FAIL → DO NOT ADVANCE

COMPONENT–PERMIT–MAINTENANCE LINKS TO DRAW

B01–03

route/shade/staff

daily; retain

A01–03

bay/cabinet/terminal

before trial; remove

E01–03

state/e-stop/receipt

open/close review; retain panel

MAT-01–05

dry frame/screen/base/paving/panel

specialist review; reversible

RESPONSIBILITY + NEXT GATE

01

VENUE LEAD

PENDING

02

BASELINE SERVICE

PENDING

03

SAFETY LEAD

PENDING

04

DATA RECORDER

PENDING

CURRENT G0 • SURVEY + PERMIT PREP

PENDING_MARKET_QUOTE • NOT BUILT • NOT FIELD-RUN

EVIDENCE DESK • DESIGN CHOICE → PREPARATION → FIELD MEASUREMENT

Unknowns stay blank; G0 is the next step, not the hero

01

DESIGN CHOICE

ALT-A / REJECT

cuts public cross; fire/removal conflict

ALT-B / REVISE

routes stay; supervision/removal fragment

ALT-C / ADVANCE

one-side bay; 4 m route across four states

GEOMETRY AUDIT

21 hard gates; computation is not field performance

02

IMPLEMENTATION PREP

CURRENT G0

enter survey and permit preparation

EIGHT PERMITS

site/fire/access/power/network/traffic/equipment

FOUR POSTS

venue, baseline, safety, data

90-DAY FIVE GATES

failure returns to ordinary opening

03

FIELD MEASUREMENT

12 CONTRACTS

denominator, sample, owner, stop, recovery defined

FIELD RESULTS

0; footfall, safety, efficiency, energy unknown

BLANK RECEIPT

human committee fills adopt / revise / stop

EXIT + RESTORE

clock defined; duration awaits drill

Prices remain formulas only; failed permit, post, baseline or removal drill blocks AI trial.

Synthetic checks test rule consistency only; published facts, design assumptions and field unknowns remain separate.
